ID		Task Mode	Task Name	Duration	Start
1	✓		Preconstruction Conference	1 day	Fri 12/20/19
2			NTP	0 days	Fri 12/20/19
3	✓		Mobilization	1 day	Mon 1/6/20
4			**Phase I - East Allen Rd to Miller**	**127 days**	**Tue 12/17/19**
5	✓		Wide Area conference	0 days	Tue 12/17/19
6			Traffic control	2 days	Mon 1/6/20
7	✓		Install Fence	2 days	Wed 1/8/20
8	✓		Milling Surface	2 days	Mon 1/13/20
9	✓		Remove Concrete	8 days	Wed 1/15/20
10	✓		Remove Elect Signals	0 days	Fri 1/10/20
11			**WaterLine**	**26 days**	**Mon 1/27/20**
12			Install Water Line, 975 LF allen to miller	12 days	Mon 1/27/20
13			Install Water Line Wall street 147 LF	2 days	Wed 2/12/20
14			Install 10" Waterline Orchard Street 165 LF	2 days	Fri 2/14/20
15			Chlorinate and Test Waterline	2 days	Tue 2/18/20
16			Bac- Test Waterline	1 day	Thu 2/20/20
17			Tie in New waterline to Existing	1 day	Fri 2/21/20
18			Cut over New Water line Services, 41 services	6 days	Mon 2/24/20
19			**StormDrain**	**34 days**	**Wed 2/12/20**
20			Install New Storm Drain, 36" HDPE, 504.39 LF	4 days	Wed 2/12/20
21			Install New Storm Drain, 30" HDPE, 302.2 LF	3 days	Tue 2/18/20
22			Install New Storm Drain, 24" HDPE, 302.85 LF	3 days	Fri 2/21/20
23			Install New Storm Drain, 18" HDPE, 353.92 LF	4 days	Wed 2/26/20
24			Build Manholes, 6 each 4' Dia, 4 each 6' Dia, 1 each 7' Dia, 9 each 8' Dia	14 days	Tue 2/18/20
25			Build New Inlets, 11 each Curb inlets, 4 each surface, 20 each double curb	20 days	Tue 3/3/20
26			Build New LID's	15 days	Tue 2/18/20
27			New Curb and Gutter	15 days	Thu 3/12/20
28			Build New SW Scuppers	8 days	Thu 4/2/20
29			Subgrade prep for pavers	7 days	Thu 4/2/20
30			New Sidewalk	15 days	Tue 4/14/20
31			Build new planters	9 days	Thu 4/23/20
32			Build new Concrete ret Walls	11 days	Wed 5/6/20
33			Remove Concrete SW from Building	5 days	Thu 5/21/20
34			New SW building	10 days	Thu 5/28/20
35			Install New Pavers	24 days	Thu 4/23/20
36			Build New Concrete collars, MH, FH, Valves	12 days	Mon 3/9/20
37			Install New Irrigation Conduit and wiring	15 days	Thu 4/2/20
38			Install new Electrical Conduit and wiring	10 days	Thu 4/2/20
39			Install Sleeves (Elect & Irrigation)	5 days	Thu 4/2/20
40			Subgrade Prep	5 days	Thu 4/23/20
41			Base course	5 days	Thu 4/30/20
42			Apshalt Pave	5 days	Thu 5/7/20
43			Stripe	5 days	Thu 5/14/20
44			Install new Lights & Appurtaences	13 days	Thu 4/16/20
45			EOPhase I	0 days	Wed 6/10/20
46			**Phase II - West Allen Rd to Auburn**	**103 days**	**Thu 6/11/20**
47			Wide Area conference	1 day	Thu 6/11/20
48			Traffic control	2 days	Fri 6/12/20

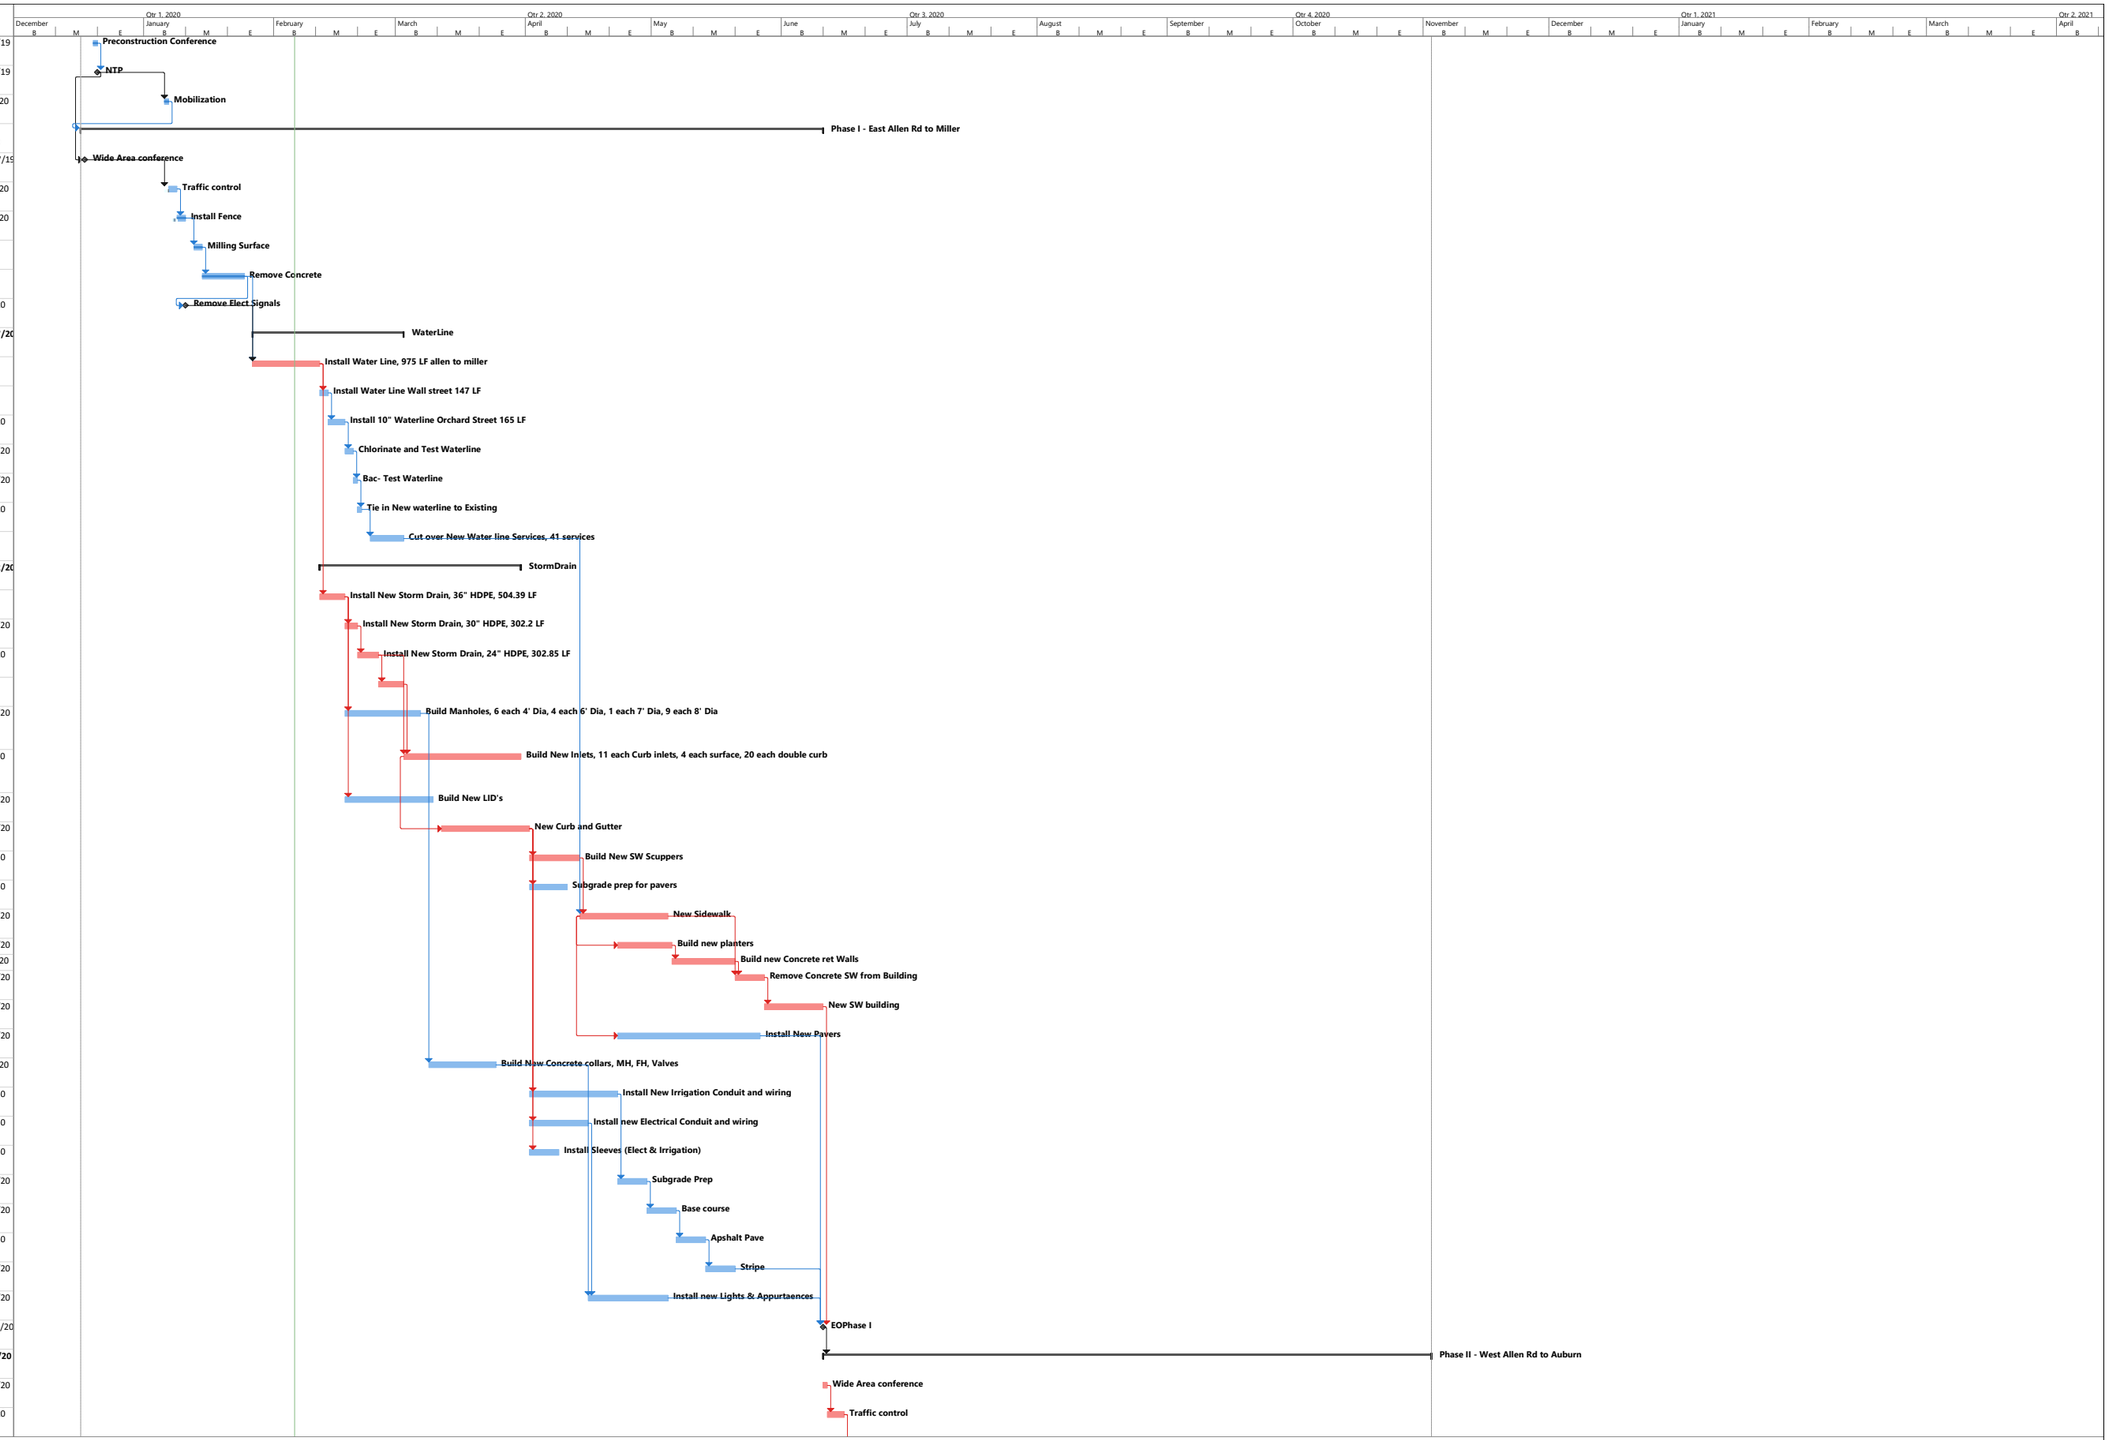

Project: 103002020 Schedule Fa
Date: Thu 2/6/20

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Mode	Task Name	Duration	Start
49		Install Fence	2 days	Tue 6/16/20
50		Milling Surface	2 days	Thu 6/18/20
51		Remove Concrete	7 days	Mon 6/22/20
52		Remove Electrical Signals	2 days	Tue 6/16/20
53		**Install Waterline Phase II**	**29 days**	**Wed 7/1/20**
54		Install Waterline Main St, 1154.55 Allen to Auburn	10 days	Wed 7/1/20
55		Install Water Line Allen street 163 LF 8" WL	2 days	Wed 7/15/20
56		Install 8" Waterline Behrend Street 103.81 LF WL South, 22' North	1 day	Fri 7/17/20
57		Install 8" Waterline Locke Street 105.05 LF WL North	1 day	Mon 7/20/20
58		Chlorinate and Test Waterline	2 days	Tue 7/21/20
59		Bac- Test Waterline	1 day	Thu 7/23/20
60		Tie in New waterline to Existing	1 day	Fri 7/24/20
61		Cut over New Water line Services, 41 services	11 days	Mon 7/27/20
62		**Stormdrain**	**42 days**	**Wed 7/15/20**
63		Install New Storm Drain Allen 36" HDPE, 359.38 LF	4 days	Wed 7/15/20
64		Install New Storm Drain, 24" HDPE, 100.2 LF Main @ Allen	2 days	Tue 7/21/20
65		Install New Storm Drain, 36" HDPE, 338.81 LF BEHREND	4 days	Thu 7/23/20
66		Install New Storm Drain, 18" HDPE, 266.32 LF Main st at BEHREND	4 days	Wed 7/29/20
67		Install New Storm Drain, 24" HDPE, 83.69 LF, 224.62 LF 18" HDPE Main st @Locke	4 days	Tue 8/4/20
68		Install New Storm Drain, 36" HDPE, 106.40 LF Locke st, 24" HDPE, 74.20 LF Locke, 18" HDPE 30 LF at Main	4 days	Mon 8/10/20
69		Install New Storm Drain, 18" HDPE, 72.02 LF Main st @Auburn	1 day	Fri 8/14/20
70		Install New Storm Drain, 48" HDPE, 173.00 LF Auburn, 24" HDPE, 74.28 LF Auburn, 18" HDPE 47.44 LF @ Main	4 days	Mon 8/17/20
71		Build Manholes, 6 each 4' Dia, 4 each 6' Dia, 1 each 7' Dia, 9 each 8' Dia	16 days	Tue 7/21/20
72		Build New Inlets, 11 each Curb inlets, 4 each surface, 20 each double curb	19 days	Mon 8/17/20
73		Build New LID's Allen	6 days	Tue 7/21/20
74		Build New SW Scuppers	7 days	Mon 8/31/20
75		New Curb and Gutter	14 days	Wed 8/26/20
76		Subgrade prep for pavers	7 days	Tue 9/15/20
77		New Sidewalk	15 days	Wed 9/9/20
78		Build new planters	10 days	Fri 9/18/20
79		Build new Concrete ret Walls	10 days	Fri 10/2/20
80		Remove Concrete SW from Building	5 days	Fri 10/16/20
81		New SW building	10 days	Tue 10/20/20
82		Install New Pavers	24 days	Tue 9/15/20
83		Build New Concrete collars, MH, FH, Valves	10 days	Wed 8/12/20
84		Install New Irrigation Conduit and wiring	15 days	Tue 9/15/20
85		Install new Electrical Conduit and wiring	10 days	Tue 9/15/20
86		Install Sleeves (Elect & Irrigation)	4 days	Tue 9/15/20
87		Subgrade Prep	5 days	Tue 10/6/20
88		Base course	5 days	Tue 10/13/20
89		Apshalt Pave	5 days	Tue 10/20/20
90		Stripe	5 days	Tue 10/27/20
91		Install new Lights & Appurtenances	13 days	Tue 9/29/20
92		EOPhase II	0 days	Mon 11/2/20

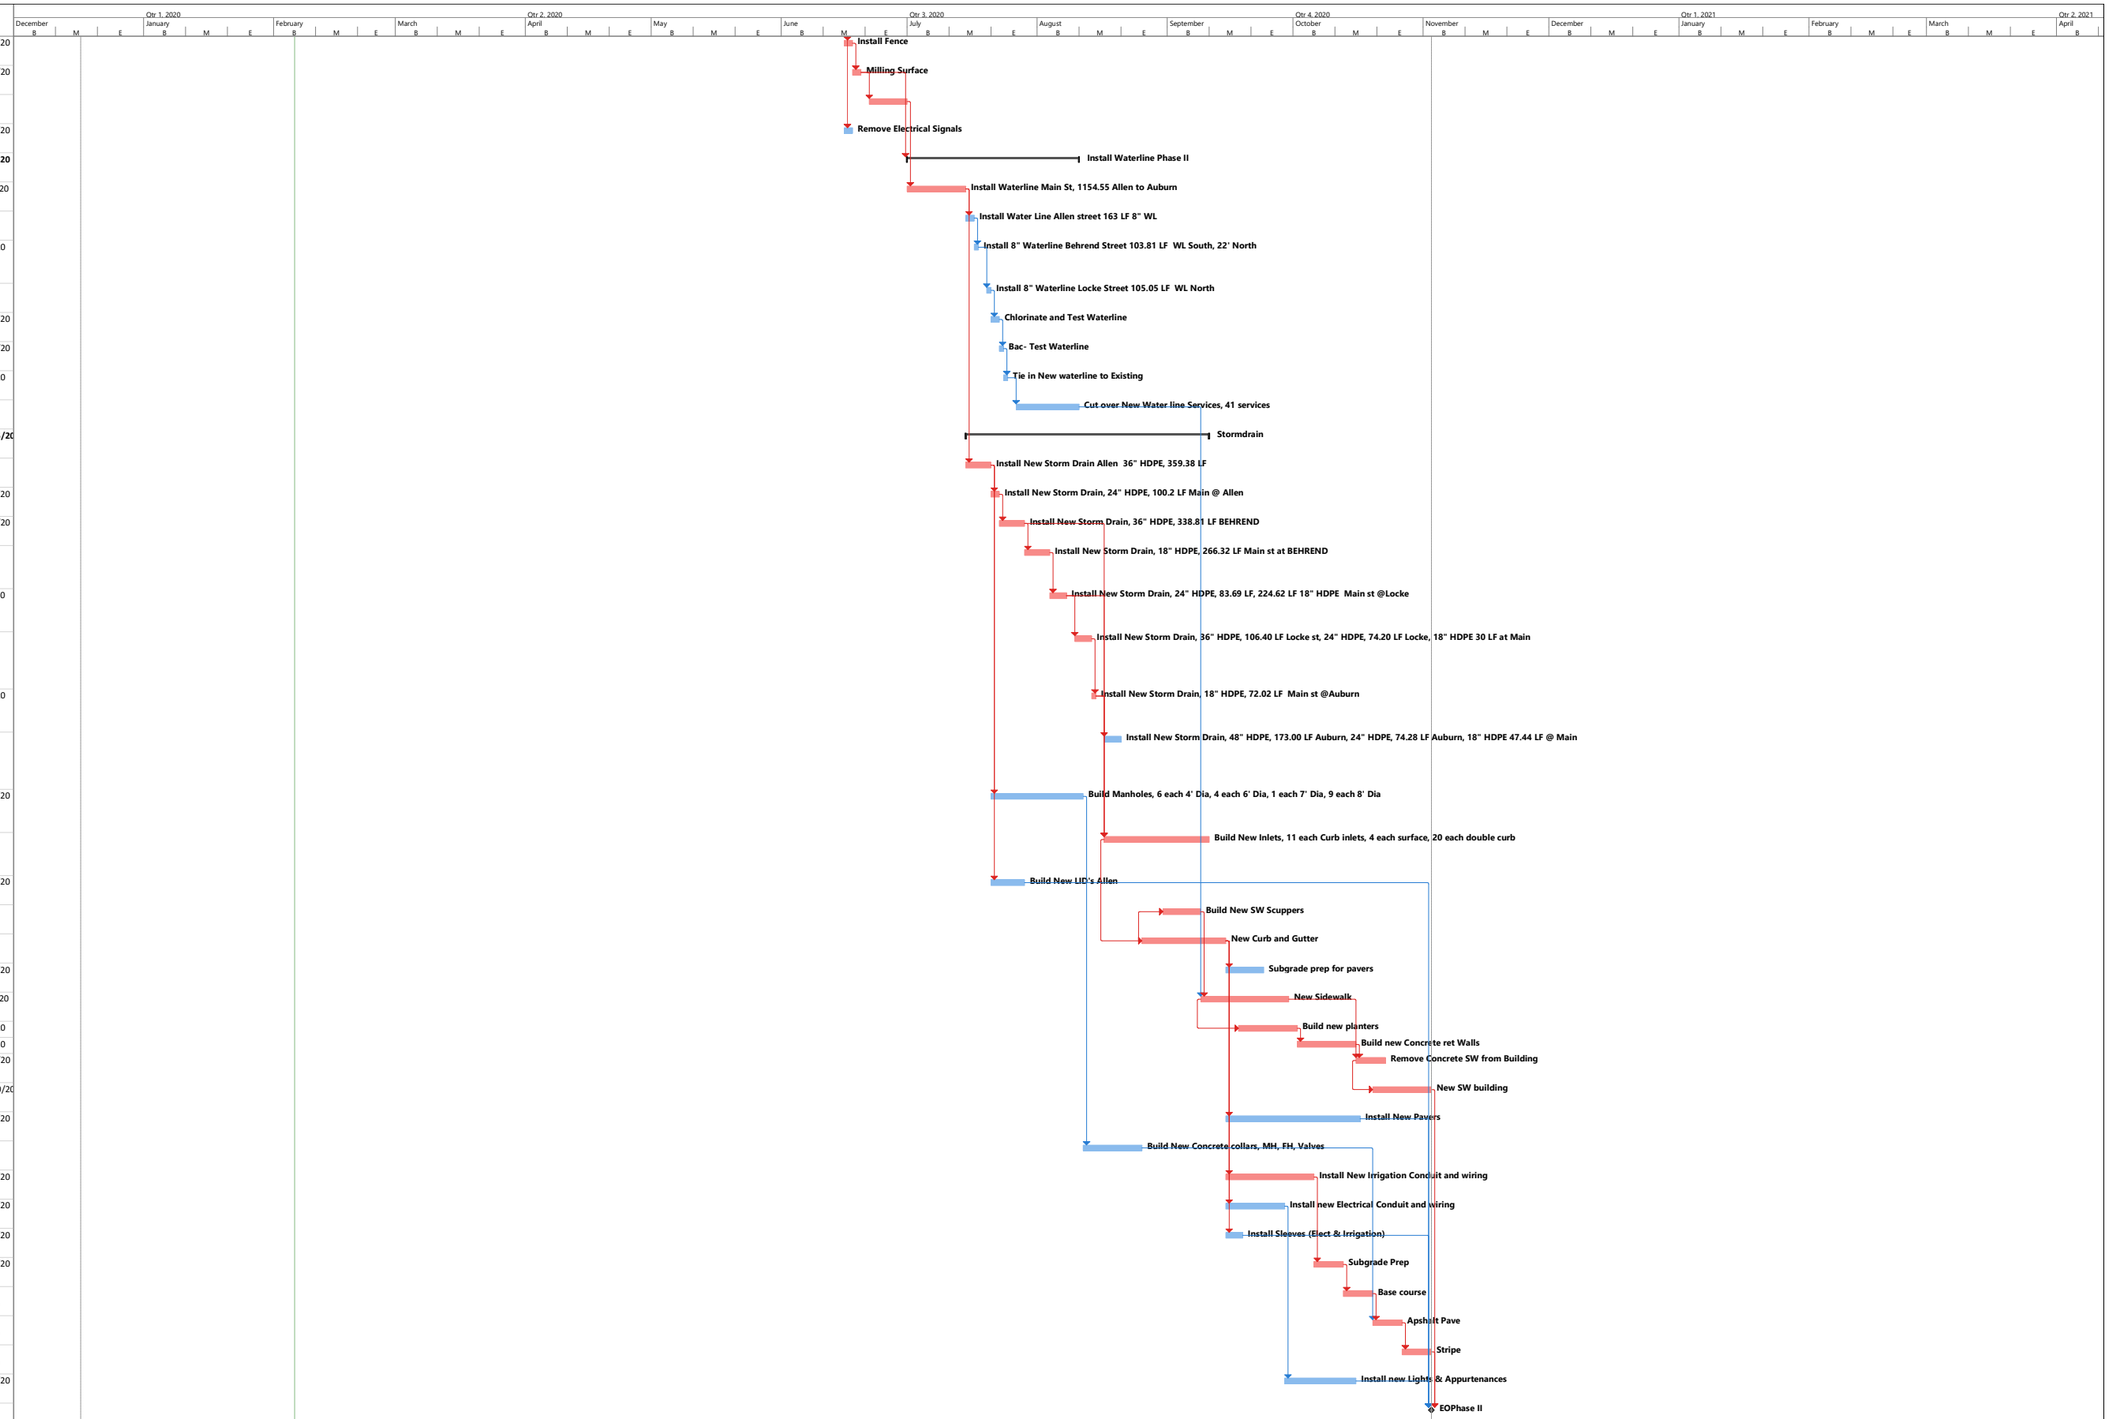

Project: 103002020 Schedule Fa
Date: Thu 2/6/20

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
